

# ***West Street Reconstruction Project***

Public Informational Meeting

April 9, 2015 – 7:00 PM

Parker Middle School Auditorium

45 Temple Street, Reading, MA

# **Anticipated Project Milestones**

# Phase 1

## Longwood Road to Winslow Road / King Street



## **Phase 1**

### **Longwood Road to Winslow Road / King Street**

- Install New Drainage  
- *May to July 2015*
- Reclaim/Grade Roadway, Install Base Layers of Pavement  
- *July to August 2015*
- Install Granite Curb, Concrete Sidewalks, and Electric Conduit  
- *August to November 2015*
- Install Final Layer of Pavement – *Spring 2016*
- Install Final Pavement Markings – *Spring 2016*

## Phase 2

# Winslow Road / King Street to Lewis Street / Scotland Road



## **Phase 2**

### **Winslow Road / King Street to Lewis Street / Scotland Road**

- Install New Drainage  
- *July to October 2015*
- Reclaim/Grade Roadway, Install Base Layers of Pavement  
- *October to November 2015*
- Install Granite Curb, Concrete Sidewalks, and Electric Conduit  
- *November to December 2015*  
- *March to May 2016*
- Install Final Layer of Pavement – *May 2016*
- Install Final Pavement Markings – *May 2016*

# Phase 3

## Lewis Street / Scotland Road to Woburn Town Line



## **Phase 3**

### **Lewis Street / Scotland Road to Woburn Town Line**

- Install New Drainage
  - *October to November 2015*
  - *March to April 2016*
- Reclaim/Grade Roadway, Install Base Layers of Pavement
  - *March to May 2016*
- Install Granite Curb, Concrete Sidewalks, and Electric Conduit
  - *May to August 2016*
- Install Final Layer of Pavement – *August 2016*
- Install Final Pavement Markings – *September 2016*

## **Traffic Signal Improvements**

- Woburn Street at Summer Avenue (NEW)  
- *September to November 2015*
- West Street at Willow Street (NEW)  
- *September to November 2015*
- West Street at Winslow Road / King Street (NEW)  
- *September to November 2015*

## **Traffic Signal Improvements (cont.)**

- West Street at Woburn Street / Wescroft Road (NEW)  
*- March to May 2016*
- West Street at South Street  
*- May 2016*

## **Miscellaneous Items**


- Complete Landscaping, Loaming, and Seeding (All phases)  
- *August to September 2016*
- Complete Final Punch List Items  
- *November to April 2017*
- Anticipated Project Completion  
- *April 2017*

# **Detours**



## DETOUR 2

- Summer Ave. to Woburn St.
- Police Dept. will evaluate detour routes for adjustments if necessary

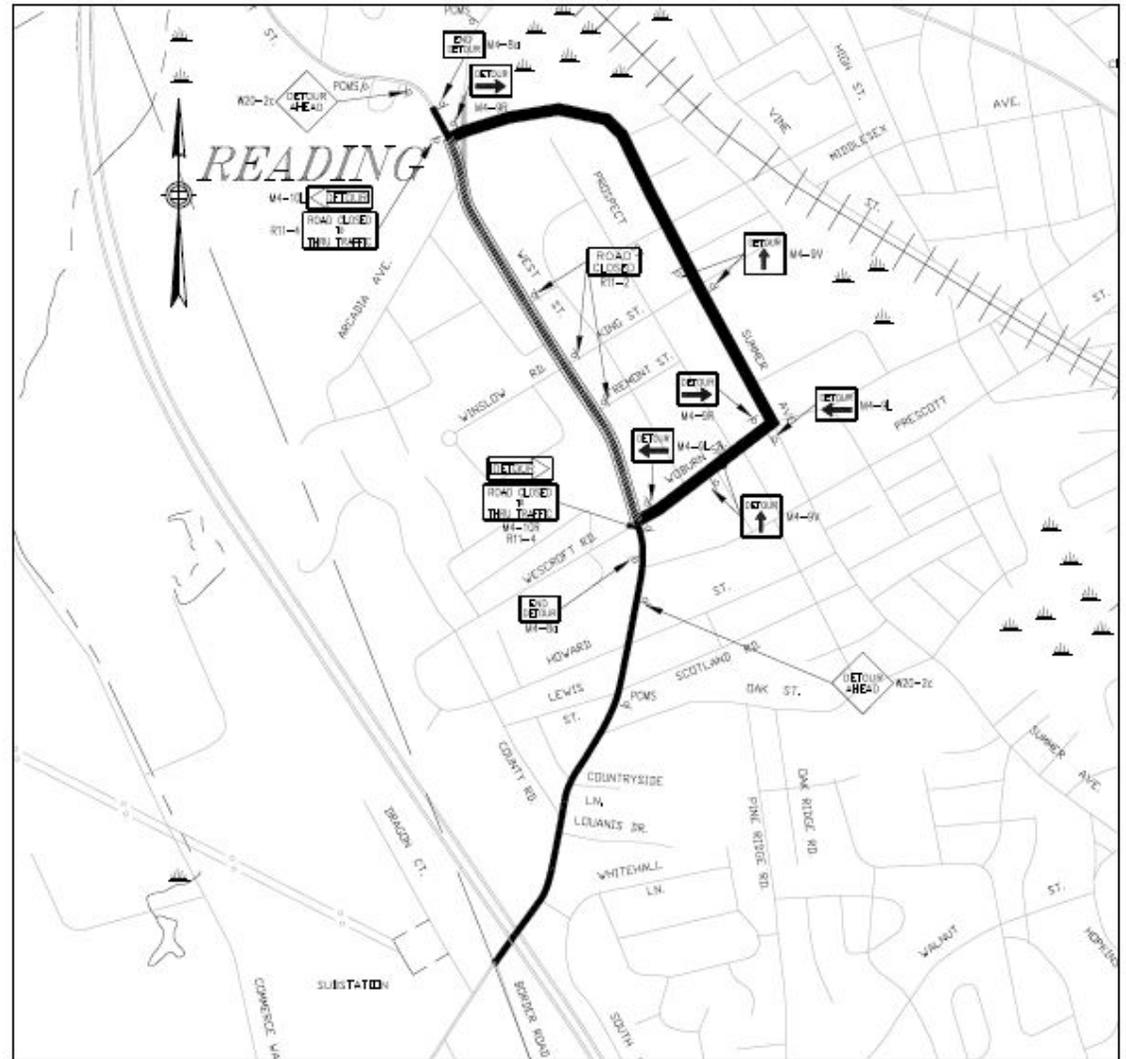

# Project Updates

- Town of Reading Website – [www.readingma.gov](http://www.readingma.gov)
  - Click on Departments
  - Click on Public Works
  - Click on Engineering Division
  - Click on “*West Street Road Improvements*”
  
- Weekly / Bi-weekly Project Update Meetings
  - 11:00 AM – Reading Town Hall, 16 Lowell Street

## Contact Information

- George Kavalaris – MassDOT Resident Engineer
  - Email: [george.kavalaris@state.ma.us](mailto:george.kavalaris@state.ma.us)
  
- George Zambouras, P.E. – Reading Town Engineer
  - Phone: 781-942-6683
  - Email: [gzambouras@ci.reading.ma.us](mailto:gzambouras@ci.reading.ma.us)
  
- Christopher Cole – Reading Staff Engineer
  - Phone: 781-942-6685
  - Email: [ccole@ci.reading.ma.us](mailto:ccole@ci.reading.ma.us)
